



Invoice

Date	Invoice #
7/8/2015	5964

Bill To
LAKE COUNTY PUBLIC WORKS PO BOX 7800 TAVARES, FL 32778

RECEIVED
 JUL 10 2015
 LAKE COUNTY
 ROAD OPERATIONS

Project Description	GUARDRAIL REPAIR
Contract #	
Financial Project #	G3047-F
Dates of Service/ Date of Completion	
Location	CR 561

Work Order No	
---------------	--

Item No	Quantity	Description	U/M	Unit Price	Total
MISC LF	25	RE-ALIGN GUARDRAIL	LF	3.00	75.00
MISC LF	25	GUARDRAIL PANEL	LF	9.00	225.00
MISC EACH	5	OFFSET BLOCKS	EA	8.00	40.00
MISC LF	25	REMOVAL	LF	1.00	25.00
MISC SY	2	MISC PAVING	sqyd	21.00	42.00

JK 10/1/15

RECEIVED
 JUL 10 2015
 LAKE COUNTY
 PUBLIC WORKS DEPARTMENT

OK TO PAY - FY 14/15

PO#: 20150045
 Acct#: 1120.5053200.830467
 Goods Recd: 7/29/15

CONTRACTOR'S SIGNATURE:

Balance Due

\$407.00

**FDOT DBE CERTIFIED
 PALM BEACH COUNTY SWBE CERTIFIED**

BP 9/30/15

KK 07.1015



LAKE COUNTY
FLORIDA

To: Southeast Guardrail & Attn., Inc. From: Public Works Road Operations Div.
 Fax: (561) 792-9798 Phone: (352) 343-6439
 Phone: (561) 792 -0040 Date: 4/14/2015
 E-Mail: csinkusga@aol.com Pages: 3

Re: 11-0604, Guardrail / Handrail Repair Service Request

WORK QUOTE REQUEST

Road Name: CR 561 Segment Number: 2-3047-09

Guardrail Number: G3047-F

Location: East shoulder on CR 561 south of Holman Lee Road

Nearest City: _____

Section: 8 Township: 21 Range: 26

Length of damage if not an end: 25' feet

Ends damaged? Yes No

If yes, how many? _____

Comments: Repair asphalt base as needed

Questions should be addressed and agreed upon in writing by either the Project Manager or designee prior to the performance of work.

Approved by: Robert Baker Date: 4-14-2014

County Representative

Work completed OK to Pay Date :	Invoice #	
Approved by:	Goods Received	

BP
4/14/15

**Guardrail
Work Quote Request**
All prices include installation

Project Name and Location

Contractor

G3047-F, CR 561

SEA

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	TOTAL PRICE
1.	Resetting Guardrail (Single Face)		LF	\$	\$
2.	Resetting Guardrail (Double Face)		LF	\$	\$
(3)	Re-alignment of existing guardrail	25	LF	\$ 3	\$ 75.00
4.	New Guardrail-Including Post, Offset Blocks, Reflectors, Delineator Assemblies, Hardware etc.		LF	\$	\$
(5)	Guardrail Panels	25	LF	\$ 9	\$ 225.00
6.	Guardrail Posts		EA	\$	\$
7.	Encased Guardrail Post		EA	\$	\$
(8)	Offset Blocks	5	EA	\$ 8	\$ 40.00
9.	Special End Shoes		EA	\$	\$
10.	Terminal Connector		EA	\$	\$
11.	Flared End Section		EA	\$	\$
12.	Half Rounded End Section		EA	\$	\$
13.	Full Rounded Buffer End Section		EA	\$	\$
14.	Anchor Plate Assembly		EA	\$	\$
15.	Type II End Anchorage Assembly		EA	\$	\$
16.	End Anchorage Assembly Type MELI		EA	\$	\$
17.	End Anchorage Assembly Type CRT		EA	\$	\$
18.	End Anchorage Assembly Type ET-2000		EA	\$	\$
19.	End Anchorage Assembly Type SRT-350 (8 post system)		EA	\$	\$
20.	End Anchorage Assembly Type BPSI		EA	\$	\$
21.	End Anchorage Assembly Type LFI		EA	\$	\$
22.	End Anchorage Assembly Type SKI-350		EA	\$	\$
23.	End Anchorage Assembly Type FLAT-350		EA	\$	\$
24.	End Anchorage Assembly Type RIGLI		EA	\$	\$
25.	Repair Existing Bridge End Assembly		EA	\$	\$
26.	Steel Anchor Post (Bridge)		EA	\$	\$
27.	Concrete Anchor Post (Bridge)		EA	\$	\$
28.	End Post with Special End Shoe Recess (Bridge)		EA	\$	\$
29.	Special Steel Guardrail Post for Single or double face Guardrail (where culverts or other structures precludes Normal installation).		EA	\$	\$
30.	Transition Panel from tri-beam to w-beam		EA	\$	\$
31.	Detail J Bridge Anchorage		EA	\$	\$
32.	ET 2000 Extruder Head		EA	\$	\$
33.	SKI 350 Extruder Head		EA	\$	\$
34.	FLAT 350 Extruder Head		EA	\$	\$
35.	Reflectors		EA	\$	\$
36.	4" Linear Reflective System (include the manufacture type and specifications)		EA	\$	\$
37.	6" Linear Reflective System (include the manufacture type and specifications)		EA	\$	\$

38. Brackets for Linear Reflective System		EA	\$	\$	
39. Removal/Disposal of Existing Guardrail	25	LF	1 \$ 3	\$	75.00 25
40. Special Safety Pipe Rail		LF	\$	\$	
41. Miscellaneous Asphalt Paving	2	SY	\$ 21	\$	42.00
42. Miscellaneous Concrete Paving		SY	\$	\$	
43. Shop Bent (Radius)		LF	\$	\$	
44. Miscellaneous sod installed		SI	\$	\$	

Total Guardrail Cost Quote:

\$ 407.00
Alb or
5-4-15

HANDRAIL
 Work Quote Request

Project Name and Location

n/a

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	TOTAL PRICE
1.	Posts 2" NPS (Sch. 40)		LF	\$	\$
2.	Rails 2" NPS (Sch. 40)		LF	\$	\$
3.	Rail joint splice		EA	\$	\$
4.	Handrail joint splice		EA	\$	\$
5.	Handrail 1 1/2" NPS		LF	\$	\$
6.	Handrail support bar 1"		LF	\$	\$
7.	Mounting base plates		EA	\$	\$
8.	Anchors bolts		EA	\$	\$
9.	Two rail assembly		LF	\$	\$
10.	Three rail assembly		LF	\$	\$

Total Handrail Cost Quote:

\$

Emergency Response Fee

\$

Total Project Cost Estimate:

\$ 407.00

County Representative
 Print *Brenda Press*
 Sign *B Press*
 Date *5/27/15*

Contractor Representative
 Print *DAVID M Rice*
 Sign *[Signature]*
 Date *5/4/15*

*** Please complete, sign, and return to Lake County



LAKE COUNTY
FLORIDA

To: Southeast Guardrail & Attn., Inc.	From: Public Works Road Operations Div.
Fax: (561) 792-9798	Phone: (352) 343-6439
Phone: (561) 792 -0040	Date: 4/14/2015
E-Mail: csinkusga@aol.com	Pages: 3

Re: 11-0604. Guardrail / Handrail Repair Service Request

WORK QUOTE REQUEST

Road Name: CR 561 Segment Number: 2-3047-09

Guardrail Number: G3047-F

Location: East shoulder on CR 561 south of Holman Lee Road

Nearest City: _____

Section: 8 Township: 21 Range: 26

Length of damage if not an end: 25' feet

Ends damaged? Yes No

If yes, how many? _____


Comments: Repair asphalt base as needed

Questions should be addressed and agreed upon in writing by either the Project Manager or designee prior to the performance of work.

Approved by: Robert Baker Date: 4-14-2014

County Representative

Work completed OK to Pay Date :	Invoice #	
Approved by:	Goods Received	

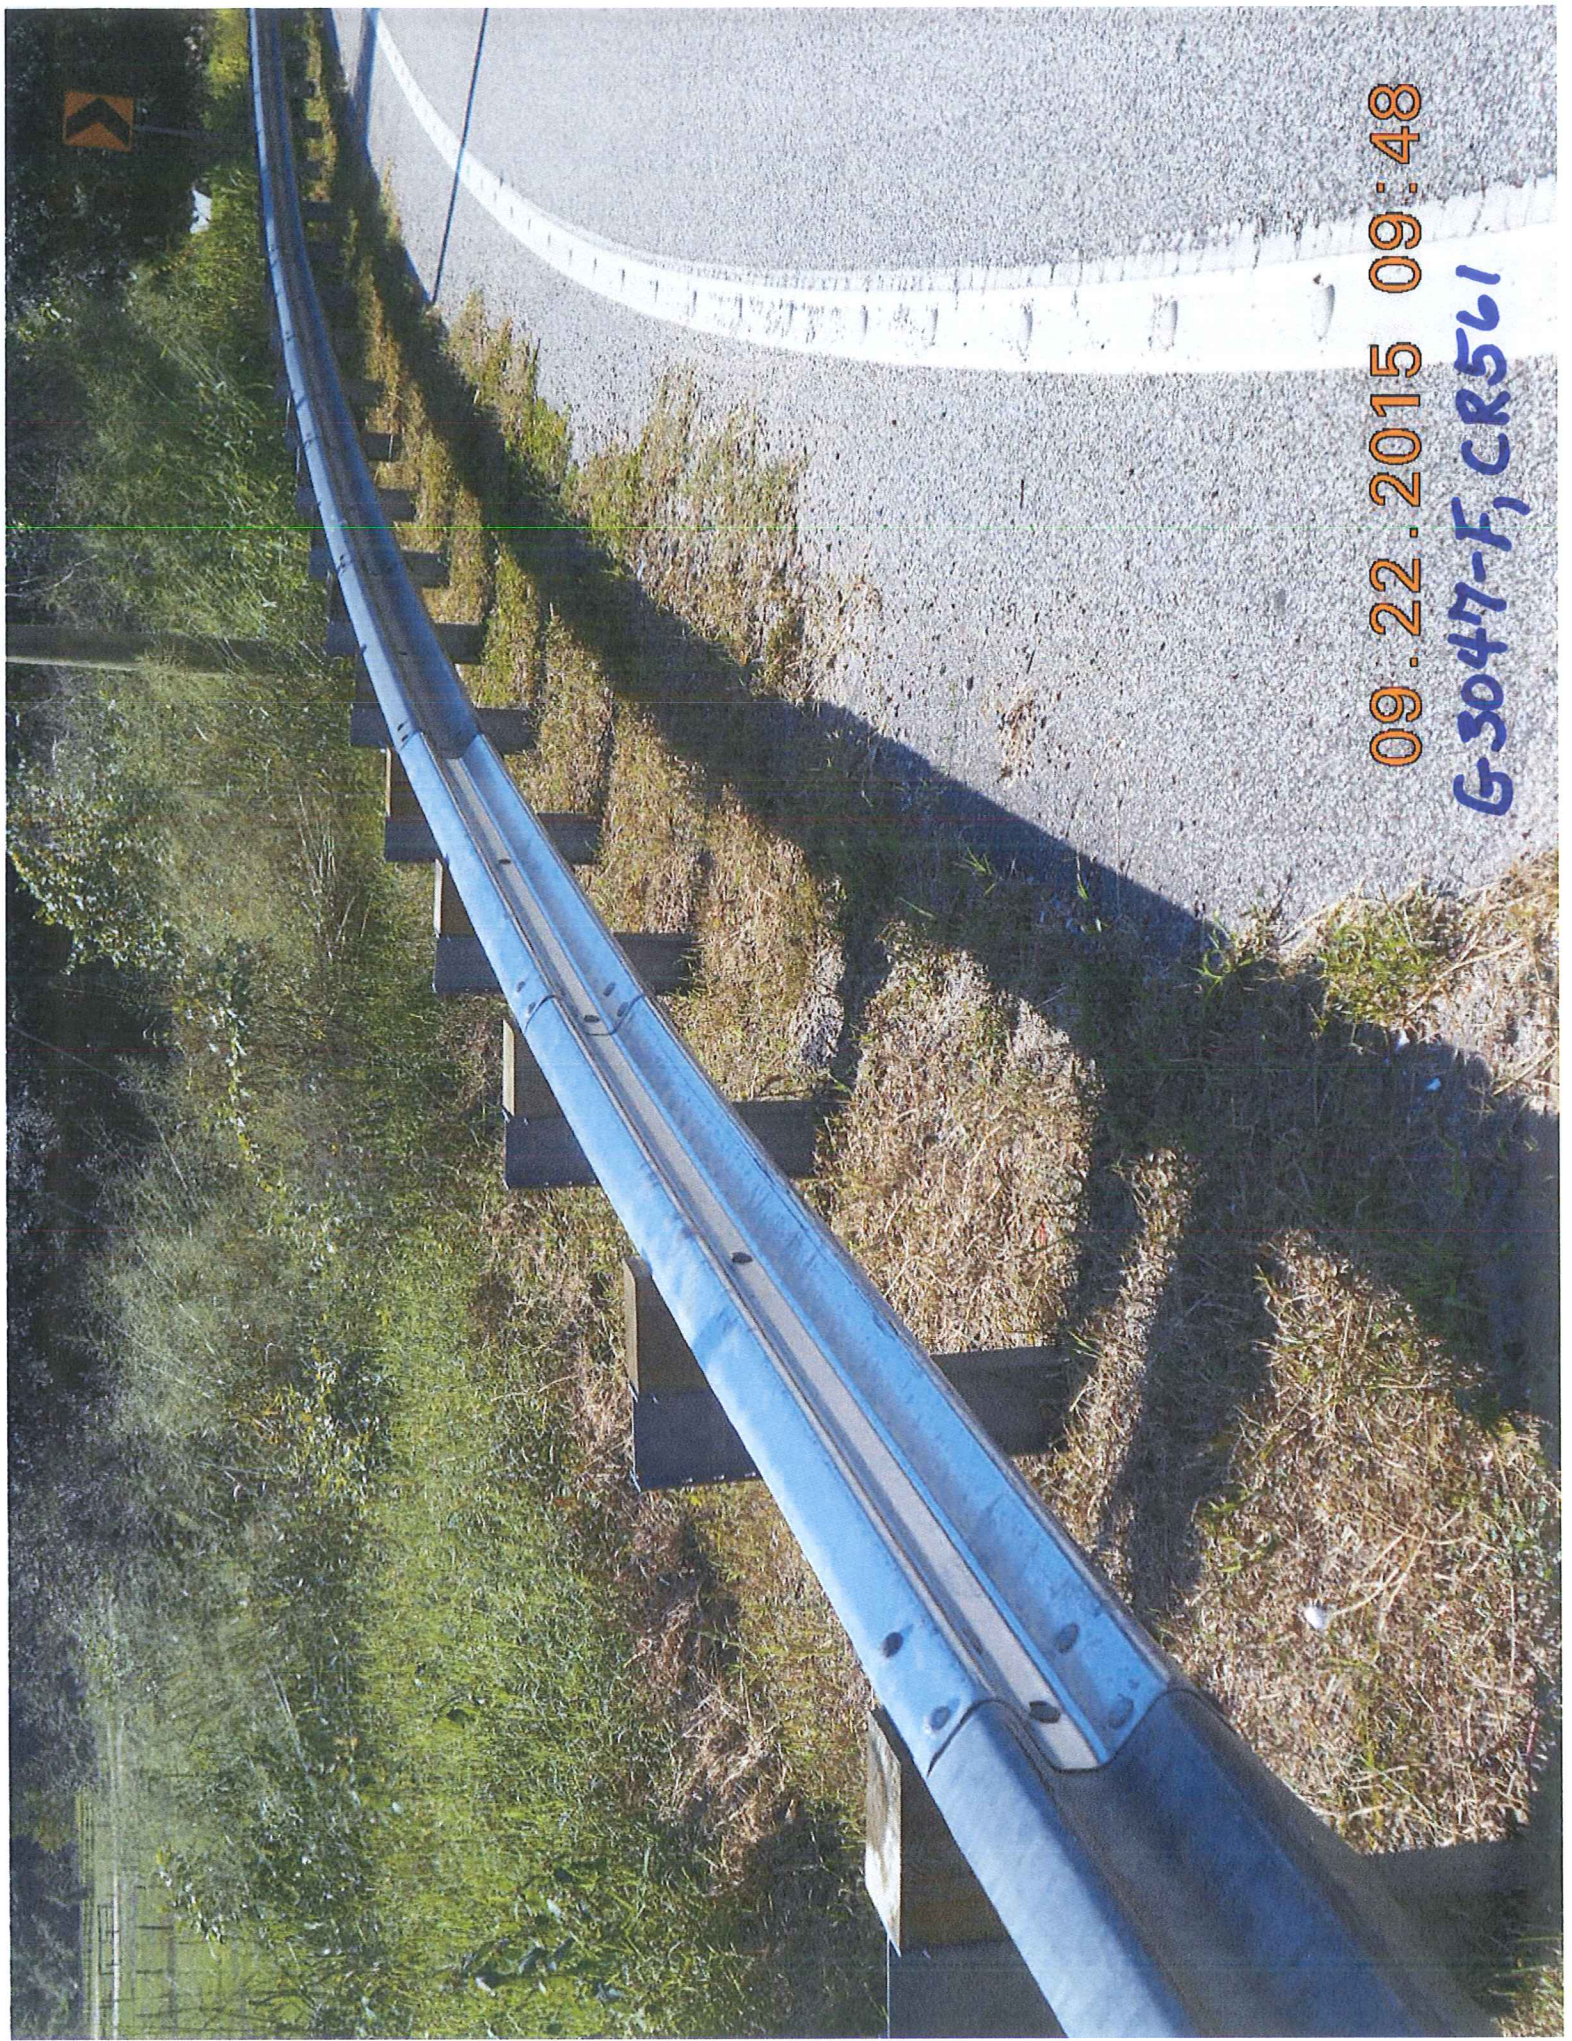

09.22.2015 09:48

G-3047-F, CR561



09:22:2015 09:48

G3047-F, CR561



04.10.2015 13:45



CR 561, G3047-F
#1, 25'

04.10.2015 13:24

Press, Brenda

From: Press, Brenda
Sent: Wednesday, July 29, 2015 8:24 AM
To: David Ricci (goquads@aol.com); 'csinkussga@aol.com'
Cc: Baker, Robert; Johnson, Jeff
Subject: Outstanding Guardrail Repairs/Invoicing

Importance: High

Good morning David,

My office received the following invoices (5962, 5963, 5964, and 5965) for the guardrails (G3047C-F) on CR 561. We cannot process these invoices at this time because the asphalt paving at the base of the posts has not been completed. The damage at the end of guardrail G3047C has not been completed either. Please coordinate with Bob Baker when these repairs are going to be completed so we can re-inspect the sites and process these invoices.

There has been another accident to the guardrail G3047C which is located in one of the newly repaired areas, which did not have the asphalt bases completed. Since the asphalt repair has not been completed, we can remove the cost for the asphalt paving from the last invoice 5963, but the work would need to be completed on all posts on the next repair. Bob will send you the paperwork for the newly damaged area, please send a quote so we can approve and possibly schedule all repairs for the same time. The repair for the new damage on guardrail G3047C will need to be quoted separately from the previous work orders.

Please call my office to discuss how you would like to proceed with resolving these outstanding issues. I will be leaving for vacation this afternoon, so if you cannot call prior to that, please speak with Bob Baker. He can be reached at (352) 343-6439 or (352) 308-9784. Thank you in advance for your assistance in resolving these outstanding items.

Brenda L. Press

Contracting Officer I

Lake County Department of Public Works, Road Ops Division

12901 County Landfill Road

Tavares, FL 32778

T: (352) 343-6439

F: (352) 742-3888

bpress@lakecountyfl.gov

Please note: Florida has a very broad public records law. Most written communication to or from government officials regarding government/public business is public record available to the public and media upon request. Your e-mail communications may be subject to public disclosure.

Press, Brenda

From: Press, Brenda
Sent: Wednesday, September 23, 2015 10:20 AM
To: Csinkussga@aol.com; David Ricci (goquads@aol.com)
Cc: Johnson, Jeff; Baker, Robert
Subject: FW: Outstanding Guardrail Repairs/Invoicing

Importance: High

Good morning David/Connie –

Please see below email that was sent back in July regarding our inability to process some of the invoices because the asphalt work was not completed. Invoice Nos. 5962 and 5964 cannot be processed as submitted because the asphalt paving was not done. Please do not submit these invoices again until the asphalt paving has been completed.

Please note that pursuant to Contract No. 11-0604C between Southeast Attenuators and Lake County there is language provided to assess the contractor a re-inspection fee of \$80 per inspection required after the initial inspection due to deficiencies or incomplete work. This language can be found in Exhibit C, General Terms and Conditions; Section 20, Final Inspection; Paragraph C.

Thank you in advance for your prompt attention to this matter.

Brenda L. Press

Contracting Officer I

Lake County Department of Public Works, Road Ops Division

12901 County Landfill Road

Tavares, FL 32778

T: (352) 343-6439

F: (352) 742-3888

bpress@lakecountyfl.gov

Please note: Florida has a very broad public records law. Most written communication to or from government officials regarding government/public business is public record available to the public and media upon request. Your e-mail communications may be subject to public disclosure.

From: Press, Brenda
Sent: Wednesday, July 29, 2015 8:24 AM
To: David Ricci (goquads@aol.com); 'csinkussga@aol.com'
Cc: Baker, Robert; Johnson, Jeff
Subject: Outstanding Guardrail Repairs/Invoicing
Importance: High

Good morning David,

My office received the following invoices (5962, 5963, 5964, and 5965) for the guardrails (G3047C-F) on CR 561. We cannot process these invoices at this time because the asphalt paving at the base of the posts has not been completed. The damage at the end of guardrail G3047C has not been completed either. Please coordinate with Bob Baker when these repairs are going to be completed so we can re-inspect the sites and process these invoices.

There has been another accident to the guardrail G3047C which is located in one of the newly repaired areas, which did not have the asphalt bases completed. Since the asphalt repair has not been completed, we can remove the cost for the asphalt paving from the last invoice 5963, but the work would need to be completed on all posts on the next repair. Bob will send you the paperwork for the newly damaged area, please send a quote so we can approve and possibly schedule

all repairs for the same time. The repair for the new damage on guardrail G3047C will need to be quoted separately from the previous work orders.

Please call my office to discuss how you would like to proceed with resolving these outstanding issues. I will be leaving for vacation this afternoon, so if you cannot call prior to that, please speak with Bob Baker. He can be reached at (352) 343-6439 or (352) 308-9784. Thank you in advance for your assistance in resolving these outstanding items.

Brenda L. Press

Contracting Officer I

Lake County Department of Public Works, Road Ops Division

12901 County Landfill Road

Tavares, FL 32778

T: (352) 343-6439

F: (352) 742-3888

bpress@lakecountyfl.gov

Please note: Florida has a very broad public records law. Most written communication to or from government officials regarding government/public business is public record available to the public and media upon request. Your e-mail communications may be subject to public disclosure.
